

**CGEWHO – CHENNAI PHASE-III  
PROJECT**



**MONTHLY PROGRESS REPORT**

**STATUS AS ON : 31.03.2024**

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

31.03.2024

BLOCK	STATUS AS ON 31 <sup>st</sup> MARCH-2024	
A1 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete 2 out of 2</li> <li>(b) Tank Wall Concrete 2 out of 2</li> <li>(c) Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Electrical Conducting works in Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank ( 2 / 2).</li> </ul> </li> </ul>	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> MARCH-2024
	<p>◆ <b>90% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Plastering 95% completed in all sides.</li> <li>▪ Fixing of Staircase Handrail 95% completed.</li> <li>▪ Fixing of Bathroom Wall Tiles 92% completed (185/200).</li> <li>▪ Fixing of Toilet Wall Tiles 92% completed (185/200).</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathrooms 92% completed (185/200)</li> <li>b) Ceramic Tiles in Toilets 92% completed (185/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 91% completed (182/200).</li> </ul>	<p>◆ <b>90% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External Plastering 95% completed in all sides.</li> <li>▪ Fixing of Staircase Handrail 95% completed.</li> <li>▪ Fixing of Bathroom Wall Tiles 94% completed (188/200).</li> <li>▪ Fixing of Toilet Wall Tiles 94% completed (188/200).</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathrooms 94% completed (188/200)</li> <li>b) Ceramic Tiles in Toilets 94% completed (188/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 94% completed (188/200).</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<p>◆ <b>Works On Progress</b></p> <ul style="list-style-type: none"> <li>▪ Water Proofing Works. <ul style="list-style-type: none"> <li>a) Terrace Water Proofing 10% completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 65% completed (130/200).</li> <li>b) Laying of Granite Countertop 75% completed (150/200).</li> <li>c) Fixing of S.S Sink 75% completed (150/200)</li> </ul> </li> <li>▪ Fixing of Door Shutters 79% completed (955/1200).</li> <li>▪ Fixing of UPVC Windows 73% completed ( 588 /800 )</li> <li>▪ Lift Materials 4 out of 4 received. Shaft work on progress.</li> <li>➤ <b>Model Flat</b> Finishing works 90% completed.</li> </ul>	<p>◆ <b>Works On Progress</b></p> <ul style="list-style-type: none"> <li>▪ Water Proofing Works. <ul style="list-style-type: none"> <li>a) Terrace Water Proofing 50% completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 94% completed (188/200).</li> <li>b) Laying of Granite Countertop 94% completed (188/200).</li> <li>c) Fixing of S.S Sink 94% completed (188/200)</li> </ul> </li> <li>▪ Fixing of Door Shutters 89% completed (1068/1200).</li> <li>▪ Fixing of UPVC Windows 74% completed ( 590 /800 )</li> <li>▪ Lift Materials 4 out of 4 received. Shaft work on progress.</li> <li>▪ Fire fighting works 15% completed.</li> <li>➤ <b>Model Flat</b> Finishing works 90% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
A2 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank <ul style="list-style-type: none"> <li>(a) Base Slab Concrete 2 out of 2</li> <li>(b) Tank Wall Concrete 2 out of 2</li> <li>(c) Top Cover slab Concrete 2 out of 2</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Electrical Conducting works upto Tenth floor.</li> <li>▪ Fixing of Water supply pipe Lines (CPVC).</li> <li>▪ Fixing of Sanitary Lines (PVC).</li> <li>▪ Fixing of Vertical Plumbing Lines in Shaft.</li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> MARCH-2024
<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of Bathroom Wall Tiles 37% completed (74/200).</li> <li>▪ Fixing of Toilet Wall Tiles 37% completed (74/200).</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 37% completed (74/200)</li> <li>b) Ceramic Tiles in Toilet 37% completed (74/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 35% completed. (70/200).</li> <li>▪ Fixing of Door Shutters 32% completed (389/1200).</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 20% completed (40/200).</li> <li>b) Laying of Granite Countertop 20% completed (40/200).</li> <li>c) Fixing of S.S Sink 20% completed (40/200)</li> </ul> </li> <li>▪ Water Proofing Work                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank 50% completed (1 / 2)</li> <li>b) Terrace Water proofing 25% completed.</li> </ul> </li> <li>▪ Lift Materials 4 out of 4 received. Shaft work on progress.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of Bathroom Wall Tiles 73% completed (146/200).</li> <li>▪ Fixing of Toilet Wall Tiles 73% completed (146/200).</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 73% completed (146/200)</li> <li>b) Ceramic Tiles in Toilet 73% completed (146/200)</li> </ul> </li> <li>▪ Vitrified Tiles in Halls &amp; Bedrooms 70% completed. (140/200).</li> <li>▪ Fixing of Door Shutters 59% completed (708/1200).</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 24% completed (47/200).</li> <li>b) Laying of Granite Countertop 24% completed (47/200).</li> <li>c) Fixing of S.S Sink 24% completed (47/200)</li> </ul> </li> <li>▪ Water Proofing Work                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank 50% completed (1 / 2)</li> <li>b) Terrace Water proofing 30% completed.</li> </ul> </li> <li>▪ Lift Materials 4 out of 4 received. Shaft work on progress.</li> <li>▪ Fire fighting works 15% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> MARCH-2024
B1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter)</li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> <li>▪ Fixing of Door Shutters 100% completed (840/840).</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BI BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 3 out 3.</li> <li>▪ Lift Cladding works 3 out of 3.</li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Fixing of M.S Window Safety Grills 90% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Firefighting works 60% completed.</li> </ul> </li> <li>• <b>Model Flat</b> Finishing works 95% completed.</li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 3 out 3.</li> <li>▪ Lift Cladding works 3 out of 3.</li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Fixing of M.S Window Safety Grills 93% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Firefighting works 75% completed.</li> <li>▪ Terrace Water supply Ring main works 50% completed.</li> </ul> </li> <li>• <b>Model Flat</b> Finishing works 95% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
B2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Upto Tenth floor level slab R.C.C</li> <li>▪ Tenth floor columns concrete.</li> <li>▪ Terrace floor level slab 1<sup>st</sup> Half R.C.C.</li> <li>▪ Parapet Columns Concrete 50% completed</li> <li>▪ Block work upto Eighth floor.</li> <li>▪ Ceiling plastering upto Seventh floor.</li> <li>▪ Wall plastering upto Seventh floor.</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Tenth floor Columns Concrete 50% completed.</li> <li>▪ Shuttering works for 2<sup>nd</sup> Half of 10<sup>th</sup> Floor level slab 90% completed.</li> <li>▪ Block work                             <ul style="list-style-type: none"> <li>a) In Eighth floor 80% completed.</li> </ul> </li> <li>▪ Ceiling Plastering                             <ul style="list-style-type: none"> <li>a) In Seventh floor 85% completed.</li> </ul> </li> <li>▪ Wall Plastering                             <ul style="list-style-type: none"> <li>a) In Seventh floor 85% completed</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Reinforcement works for 2<sup>nd</sup> Half of Terrace Floor level slab 98% completed. ( <b>Final slab Concrete planned on 5<sup>th</sup> April 2024</b>)</li> <li>▪ Block work                             <ul style="list-style-type: none"> <li>a) In Ninth floor 90% completed.</li> </ul> </li> <li>▪ Ceiling Plastering                             <ul style="list-style-type: none"> <li>a) In Ninth floor 70% completed.</li> </ul> </li> <li>▪ Wall Plastering                             <ul style="list-style-type: none"> <li>a) In Ninth floor 70% completed</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Electrical conducting works 45% completed.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Electrical conducting works 70% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
C1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Internal Plumbing Line.                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms</li> <li>c) Vitrified Tiles in Corridor 100% completed.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed.</li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank</li> <li>b) Terrace floor Water proofing.</li> </ul> </li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ Lift Cladding works 4 out of 4.</li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C1 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of Door Shutters 100% completed (1080 / 1080)</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (120/120)</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Staircase Hand Rails 3 out of 3</li> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Electrical wire pulling work 100% completed (120/120).</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 85% completed.</li> <li>▪ Fire Fighting works 40% completed.</li> </ul> </li> <li><b>Model Flat</b> Finishing works 95% completed.</li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Staircase Hand Rails 3 out of 3</li> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Terrace Water supply Ring main works 90% completed</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of M.S Window Safety Grills 85% completed.</li> <li>▪ Fire Fighting works 52% completed.</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
C2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (2 out of 3)</li> <li>(b) Wall Concrete (2 out of 3)</li> <li>(c) Top Cover slab (2 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> </ul> </li> </ul>	





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C2 BLOCK	<ul style="list-style-type: none"> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank 3 out of 3</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles completed.</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom completed.</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms completed.</li> <li>c) Vitrified Tiles in Corridor completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 120 / 120 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 120 / 120).</li> <li>c) Fixing of S.S Sink 100% completed. ( 120 / 120).</li> </ul> </li> <li>▪ Fixing of UPVC Window 100% completed. ( 600 / 600 )</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240)</li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed (1080 / 1080)</li> <li>▪ Laying of Green marble for Staircase 100% completed..</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Lift Installation works 4 out 4 - 85% completed.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 95% completed.</li> </ul> </li> <li>▪ Lift Cladding work 90% completed.</li> </ul> </li> <li>◆ <b>Works Of Progress</b> <ul style="list-style-type: none"> <li>▪ Electrical wire pulling 65% completed ( 78 /120).</li> <li>Fire fighting works 40% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Lift Installation works 4 out 4 - 85% completed.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 95% completed.</li> </ul> </li> <li>▪ Lift Cladding work 90% completed.</li> <li>▪ Electrical wire pulling 90% completed ( 109 /120).</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fire fighting works 45% completed.</li> <li>▪ Fixing of Modular Switches &amp; Sockets 55% completed. (66/120).</li> <li>▪ Terrace Water supply Ring main works 55% completed</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS AS ON 31 <sup>st</sup> MARCH-2024	
C3 BLOCK	<p>◆ <b>100% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Terrace floor level slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (2 out of 3)</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Over Head Water Tank ( 1 / 2) completed.</li> </ul> </li> <li>▪ Kitchen Finishing Works               <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed (100/100)</li> <li>b) Laying of Granite Countertop 100% completed. (100/100).</li> <li>c) Fixing of S.S Sink 100% completed. (100/ 100).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 300 /300 )</li> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. ( 300 /300 )</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 100 / 100 )</li> </ul> </li> <li>▪ Laying of Green marble for Staircase 100% completed.</li> </ul>	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> MARCH-2024
	<p>◆ <b>90% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty 90% completed. ( 90 /100 ).</li> </ul>	<p>◆ <b>90% Completed Works</b></p> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails.</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty 90% completed. ( 90 /100 ).</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

C3 BLOCK	<ul style="list-style-type: none"> <li>▪ Fixing of UPVC Window 93% Completed. ( 436 / 500 ).</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 94% completed ( 188 / 200 ).</li> <li>▪ Fixing of Main Door &amp; Internal Shutters 99% completed ( 898 / 900 ).</li> <li>▪ Water Proofing Works. <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works – <ul style="list-style-type: none"> <li>2 Lifts - 85% completed.</li> <li>3<sup>rd</sup> Lift - 25% completed.</li> <li>4<sup>th</sup> Lift - 10% completed.</li> </ul> </li> <li>▪ Lift Cladding work 40% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of UPVC Window 97% Completed. ( 487 / 500 ).</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 98% completed ( 197 / 200 ).</li> <li>▪ Fixing of Main Door &amp; Internal Shutters 99% completed ( 898 / 900 ).</li> <li>▪ Water Proofing Works. <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 95% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works – <ul style="list-style-type: none"> <li>2 Lifts - 85% completed.</li> <li>3<sup>rd</sup> Lift - 30% completed.</li> <li>4<sup>th</sup> Lift - 15% completed.</li> </ul> </li> <li>▪ Lift Cladding work 50% completed.</li> <li>▪ Electrical wire pulling 50% completed ( 50 /100).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 43% completed. (43/100).</li> <li>▪ Fire fighting works 45% completed.</li> </ul> </li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
D1 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Water Proofing Works. <ul style="list-style-type: none"> <li>a) Over Head Water Tank 3 out of 3</li> <li>b) Terrace floor Water proofing 100% completed.</li> </ul> </li> <li>▪ Fixing of Internal Plumbing Line</li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D1 BLOCK	<ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> <li>▪ Fixing of Vertical Plumbing Line in Shafts</li> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 320 / 320 ).</li> <li>▪ Laying Of Floor Tiles <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. ( 320 / 320 )</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Kitchen Finishing Works <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 80 / 80 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 80 / 80).</li> <li>c) Fixing of S.S Sink 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed ( 880 / 880 )</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 95% completed.</li> <li>▪ Application of External Wall Primer-1<sup>st</sup> Coat</li> <li>▪ Fixing of UPVC Windows 99% completed. (398 / 400).</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty 99% completed. ( 78 / 80 ).</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of UPVC French Door 98% completed.(without Mosquito mesh shutter) ( 158 / 160 )</li> <li>▪ Application of Exterior Wall Primer 80% completed</li> <li>▪ Lift Installation works <ul style="list-style-type: none"> <li>a) 3 out 4 - 80% completed.</li> <li>b) 4<sup>th</sup> lift - work on progress.</li> </ul> </li> <li>▪ Electrical Wire pulling works 12% completed. (10/ 80).</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ External plastering in all sides 95% completed.</li> <li>▪ Application of External Wall Primer-1<sup>st</sup> Coat</li> <li>▪ Fixing of UPVC Windows 99% completed. (398 / 400).</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty 100% completed. ( 80 / 80 ).</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fixing of UPVC French Door 99% completed.(without Mosquito mesh shutter) ( 159 / 160 )</li> <li>▪ Application of Exterior Wall Damp proof Paint 40% completed.</li> <li>▪ Lift Installation works <ul style="list-style-type: none"> <li>a) 3 out 4 - 80% completed.</li> <li>b) 4<sup>th</sup> lift – 10% completed.</li> </ul> </li> <li>▪ Electrical Wire pulling works 50% completed. (40/ 80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 50% completed. (40/80).</li> <li>▪ Fire fighting works 75% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

		<ul style="list-style-type: none"> <li>▪ Laying of External Sewerage lines 85% completed</li> <li>▪ Laying of External Water supply lines 90% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
D2 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (3 out of 3) - Slab Concrete.</li> <li>▪ Over Head Water Tank                             <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms.</li> <li>c) Vitrified Tiles in Corridor.</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of Main Door &amp; Internal Shutters.</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados.</li> <li>b) Laying of Granite Countertop.</li> <li>c) Fixing of S.S Sink.</li> </ul> </li> <li>▪ External Plastering in all sides.</li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D2 BLOCK	<ul style="list-style-type: none"> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank</li> </ul> </li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter).</li> <li>▪ Electrical Wire pulling works 100% completed (80/ 80).</li> <li>▪ Fixing of Modular Switches &amp; Sockets 100% completed. (80/80).</li> <li>▪ Fire Fighting Works 100% completed.</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Lift Cladding works 4 out of 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Fixing of M.S Window Safety Grills 90% completed. (290 / 320).</li> <li>▪ Electrical Wire pulling works 99% completed (79/ 80).</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Fire Fighting Works 60% completed.</li> <li>▪ <b>Model Flat</b> Finishing works 95% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Lift Cladding works 4 out of 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Fixing of M.S Window Safety Grills 90% completed. (290 / 320).</li> <li>▪ Laying of External Sewerage lines 90% completed.</li> <li>▪ Laying of External Water supply lines 90% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>▪ Laying of Storm Water drain pipes 90% completed.</li> <li>▪ Application of Exterior Wall Damp proof Paint 15% completed.</li> <li>▪ Fire Fighting Works 95% completed.</li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 95% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
D3 BLOCK	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b> <ul style="list-style-type: none"> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (4 out of 4) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete (3 out of 3)</li> <li>(b) Wall Concrete (3 out of 3)</li> <li>(c) Top Cover slab (3 out of 3 )</li> </ul> </li> <li>▪ Block work upto Tenth floor &amp; Parapet wall.</li> </ul> </li> </ul>	



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

D3 BLOCK	<ul style="list-style-type: none"> <li>▪ Ceiling Plastering upto Tenth floor.</li> <li>▪ Wall plastering upto Tenth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts                             <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Over Head Water Tank 1 out of 3</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles 100% completed. ( 320 / 320 )</li> <li>▪ Kitchen Finishing Works                             <ul style="list-style-type: none"> <li>a) Fixing of Wall Dados 100% completed. ( 80 / 80 )</li> <li>b) Laying of Granite Countertop 100% completed. ( 80 / 80).</li> </ul> </li> <li>▪ Fixing of S.S Sink 100% completed. ( 80 / 80).</li> <li>▪ Laying Of Floor Tiles                             <ul style="list-style-type: none"> <li>a) Ceramic Tiles in Bathroom 100% completed. (320 / 320)</li> <li>b) Vitrified Tiles in Halls &amp; Bedrooms 100% completed. ( 80 / 80 )</li> <li>c) Vitrified Tiles in Corridor 100% completed.</li> </ul> </li> <li>▪ Fixing of Main Door &amp; Internal Shutters 100% completed (880 / 880)</li> <li>▪ Water Proofing Works.                             <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing 100% completed.</li> <li>b) Over Head Water Tank 3 out of 3 completed.</li> </ul> </li> <li>▪ Fixing of UPVC Windows 100% completed. ( 400 / 400 )</li> <li>▪ Electrical Wire pulling works 100% completed (80/ 80).</li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Tenth floor.</li> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 99% completed ( 159 / 160).</li> <li>▪ Laying of Green marble for Staircase.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed ( 160 / 160).</li> <li>▪ Laying of Green marble for Staircase.</li> <li>▪ Lift Cladding works 90% completed.</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Lift Cladding works 90% completed.</li> <li>▪ Application of Exterior Wall Primer</li> <li>◆ <b>Works On Progress</b></li> <li>▪ Lift Installation works - 4 out of 4 - 85% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 62% completed (200/320).</li> <li>▪ Firefighting works 25% completed.</li> <li>▪ Electrical Wire pulling works 50% completed (40/ 80).</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fixing of Modular Switches &amp; Sockets 93% completed. (75/80).</li> <li>▪ Application of Exterior Wall Primer</li> <li>▪ Laying of External Sewerage lines 90% completed.</li> <li>▪ Laying of External water supply lines 90% completed.</li> <li>◆ <b>Works On Progress</b></li> <li>▪ Lift Installation works - 4 out of 4 - 85% completed.</li> <li>▪ Fixing of M.S Window Safety Grills 62% completed (200/320).</li> <li>▪ Firefighting works 75% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>	
COMMUNITY HALL	<ul style="list-style-type: none"> <li>◆ <b>100% Completed Works</b></li> <li>▪ <b>Terrace floor level</b> slab R.C.C</li> <li>▪ Terrace floor Parapet Columns Concrete.</li> <li>▪ Lift Head room (2 out of 2) - Slab Concrete.</li> <li>▪ Over Head Water Tank               <ul style="list-style-type: none"> <li>(a) Base Slab Concrete</li> <li>(b) Tank Wall Concrete</li> <li>(c) Top Cover slab Concrete.</li> </ul> </li> <li>▪ Block work upto Fourth floor &amp; Parapet wall.</li> <li>▪ Ceiling Plastering upto Fourth floor.</li> <li>▪ Wall plastering upto Fourth floor.</li> <li>▪ 1<sup>st</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ 2<sup>nd</sup> Coat Wall Putty upto Fourth floor.</li> <li>▪ Fixing of Balcony Handrail.</li> <li>▪ Fixing of Staircase Hand Rails</li> <li>▪ Fixing of Internal Plumbing Line               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (CPVC).</li> <li>b) Sanitary Lines (PVC)</li> </ul> </li> <li>▪ Fixing of Vertical Plumbing Line in Shafts               <ul style="list-style-type: none"> <li>a) Water supply pipe Lines (G.I).</li> <li>b) Sanitary Lines (PVC).</li> </ul> </li> <li>▪ Fixing of Bathroom Wall Tiles.</li> </ul>	





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Laying Of Floor Tiles               <ul style="list-style-type: none"> <li>a) Vitrified Floor Tiles in Hall &amp; rooms</li> <li>b) Ceramic Floor Tiles in Bathrooms.</li> <li>c) Kota Stone in Staircase &amp; Lobby</li> </ul> </li> <li>▪ Fixing of UPVC Windows.</li> <li>▪ Fixing of Wooden flush Door for rooms.</li> <li>▪ Fixing of Fire Safety Door for Hall Main Entrance</li> <li>▪ External Plastering in all sides.</li> <li>▪ Water Proofing Works.               <ul style="list-style-type: none"> <li>a) Terrace floor Water proofing.</li> <li>b) Over Head Water Tank.</li> </ul> </li> </ul>	
	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> MARCH-2024</b>
	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Lift Cladding works 4 out of 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Fire fighting works – Installation of Pipelines 90% completed.</li> <li>▪ Electrical Wire &amp; cables pulling work 85% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>Fixing of Sanitary fixtures.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>◆ <b>90% Completed Works</b> <ul style="list-style-type: none"> <li>▪ Lift Installation works 4 out 4.</li> <li>▪ Lift Cladding works 4 out of 4.</li> <li>▪ Application of Exterior Wall Primer.</li> <li>▪ Fire fighting works – Installation of Pipelines 90% completed.</li> <li>▪ Electrical Wire &amp; cables pulling work 90% completed.</li> <li>▪ Fixing of Modular Switches &amp; Sockets 90% completed.</li> </ul> </li> <li>◆ <b>Works On Progress</b> <ul style="list-style-type: none"> <li>Fixing of Sanitary fixtures.</li> <li>Excavation for laying of Firefighting Hydrant pipes on progress</li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**


---

STATUS AS ON 31 <sup>st</sup> MARCH-2024	
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"><li>➤ <b>Underground Sump-2 (Near D-Block)</b><ul style="list-style-type: none"><li>▪ Base Slab - R.C.C 100% completed.</li><li>▪ Sump Wall - R.C.C 100% completed.</li><li>▪ Top slab R.C.C 100% completed.</li><li>▪ Outer Wall Waterproof plastering – 100% completed.</li><li>▪ Inner Wall Waterproof plastering 90% completed.</li><li>▪ Pump room Inner plastering 100% completed.</li></ul></li> <li>➤ <b>Underground Sump-1 (Near B-Block)</b><ul style="list-style-type: none"><li>▪ Base Slab R.C.C 100% completed.</li><li>▪ Sump Wall - R.C.C 100% completed.</li><li>▪ Top slab R.C.C 100% completed.</li><li>▪ Outer Wall Waterproof plastering – 100% completed.</li><li>▪ Inner Wall Waterproof plastering – 70% completed.</li><li>▪ Pump room Inner plastering – 100% completed.</li></ul></li> <li>➤ <b>Sewage Treatment Plant-2 (Near D-Block)</b><ul style="list-style-type: none"><li>▪ Base slab – R.C.C 100% completed.</li><li>▪ STP Wall – R.C.C 100% completed.</li><li>▪ STP Top Slab – R.C.C 100% completed.</li><li>▪ STP Pump Room completed.</li><li>▪ Outer wall Waterproof plastering 100% completed.</li><li>▪ Inner Wall Waterproof plastering 90% completed.</li></ul></li> <li>➤ <b>Sewage Treatment Plant-1 (Near C3-Block)</b><ul style="list-style-type: none"><li>▪ Excavation Work completed.</li><li>▪ P.C.C for Base slab completed.</li><li>▪ Reinforcement for Base slab on progress.</li></ul></li></ul>

# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

## PHOTOGRAPHS OF WORK PROGRESS AS ON 31<sup>st</sup> MARCH 2024

**Community Hall :** Excavation for laying of Fire fighting Hydrant Pipe on progress.

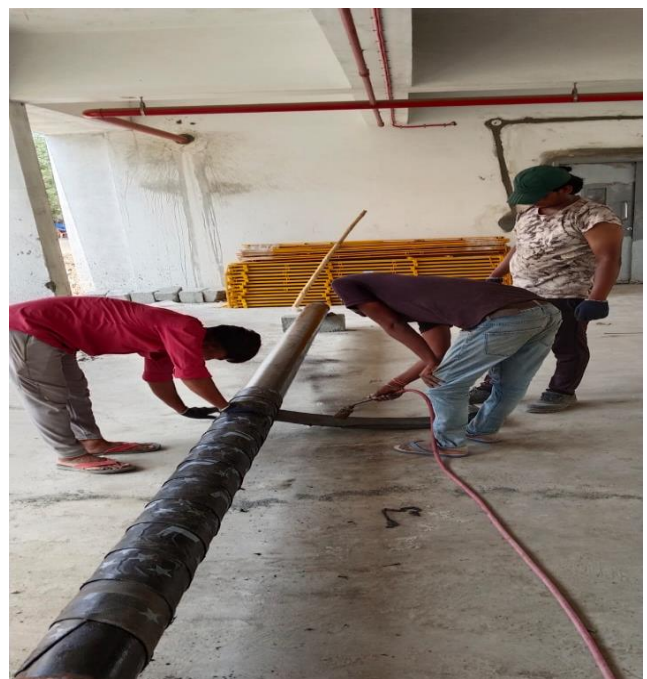


# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block A1:** Fixing of UPVC Windows, laying of flooring tiles & skirting in flats on progress.

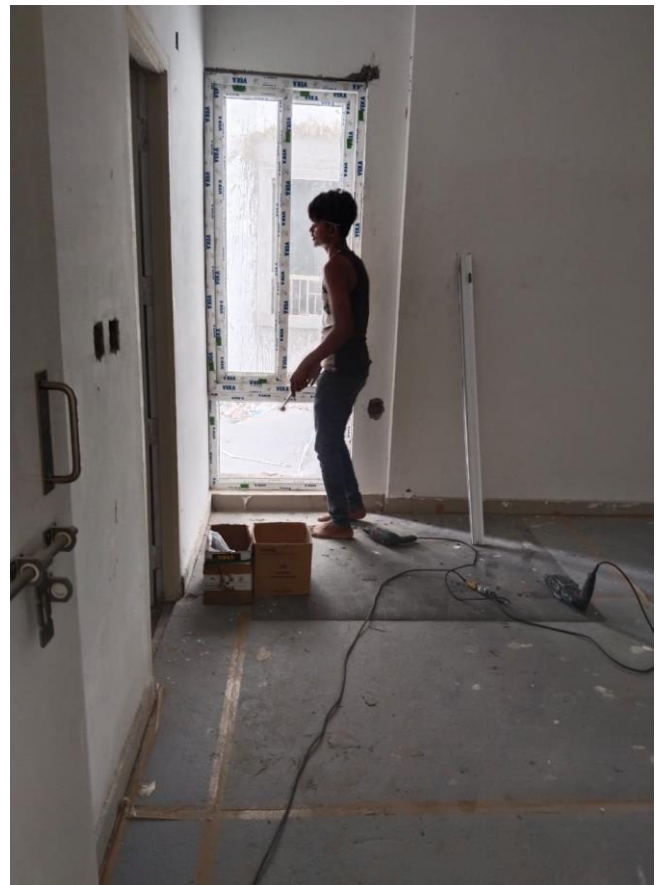

# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block A2** : Laying of bathroom & toilet floor tiles, vitrified tiles on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block B1:** Connection of Water Supply Ring main works in Terrace floor on progress.




# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block B2 :** Terrace Floor Level slab 1<sup>st</sup> half Concrete casting 100% completed. Parapet columns 50% completed. Shuttering works for 2<sup>nd</sup> half of Terrace floor level slab 98% completed (Slab concrete planned on 5<sup>th</sup> April 2024). Block work & Inner Plastering works on progress.

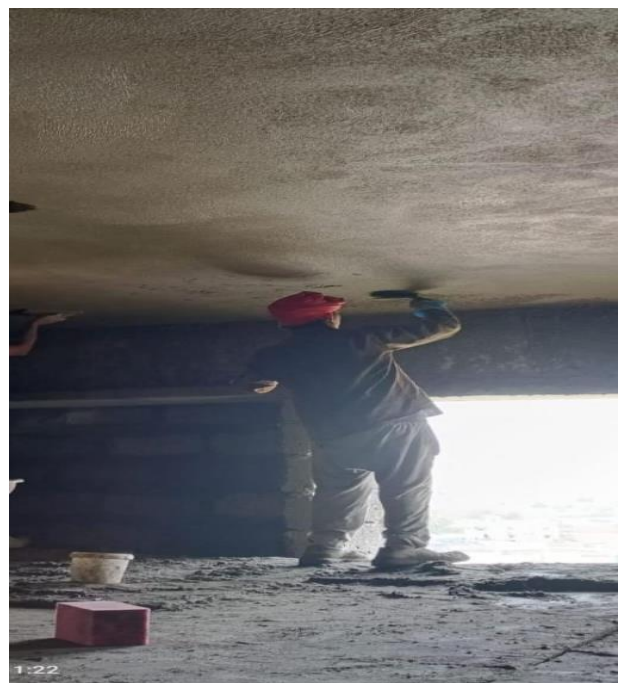

# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C1:** Firefighting works Hydrant works in Stilt floor on progress. Laying of External Sewerage lines on progress.





# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block C2:** Firefighting works Hydrant works in Stilt floor on progress. Marking for excavation for laying of External Sewerage lines on progress.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block C3: Lift Erection Works in 3<sup>rd</sup> & 4<sup>th</sup> Lift on progress.**



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D1:** Internal Electrical Wire pulling works on progress. External Painting works on progress



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D2:** Finishing Touch-up works in Plumbing shafts and Outer wall on progress. External Painting works on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Block D3:** Electrical Panel room work, Fabrication & fixing of window grills on progress.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**U.G Sump 1 (Near B Block) – All RCC works completed. Internal Waterproofing work for Pump room completed.**



**U.G Sump 2 (Near D Block) – All RCC works completed. Pump room Inner plastering 100% completed & Internal Water proof plastering works 90% completed..**



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**Sewage Treatment Plant 2 (Near D Block).** All RCC works completed. Internal Water proof plastering works 90% completed.



**Sewage Treatment Plant 1 (Near C Block).** Earthwork excavation completed. Reinforcement works for Base slab on progress.



# PROGRESS REPORT

## CGEWHO – CHENNAI PHASE-III PROJECT

---

**External Sewerage Lines :** Laying of External Sewage line & construction of Chambers around D1,D2,D3 Block & Community hall completed. Excavation works for connection of final chamber to STP on progress.



Excavation for laying of Sewer lines in C1-Block on progress.





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

**QUALITY CONTROL**

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:**

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**PHOTOGRAPH OF QUALITY CONTROL AT SITE**

**Concrete Cube Compressive Strength Testing**



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**20mm & 12mm Aggregate Sieve Analysis Testing**



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Fine Aggregate Sieve Analysis Testing**

